


# “Nouveau Centre” Project Update





Document GC/64/7


Lyon, 12-13 May 2022

International Agency  
for Research on Cancer

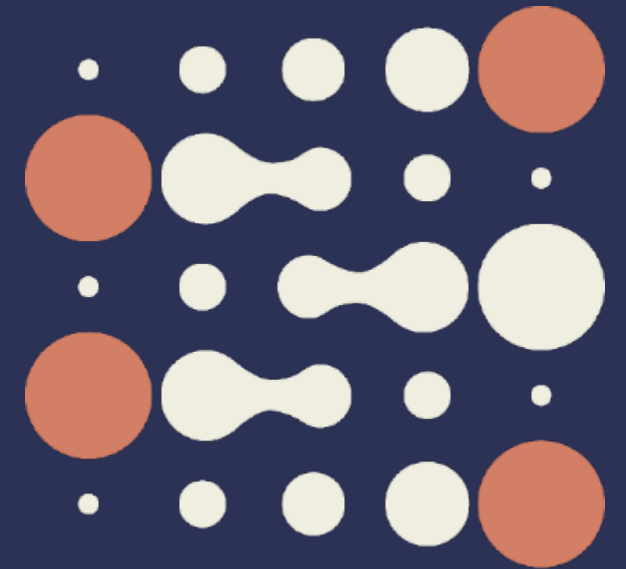


# Operational timeline




  
Inauguration

Due to overall delays, the timeslot to physically move to the new premises is very tight, without any margin. Negotiations ongoing with the Grand Lyon Métropole to anticipate some equipment deliveries prior to the delivery of the keys.



# Impact on IARC activities

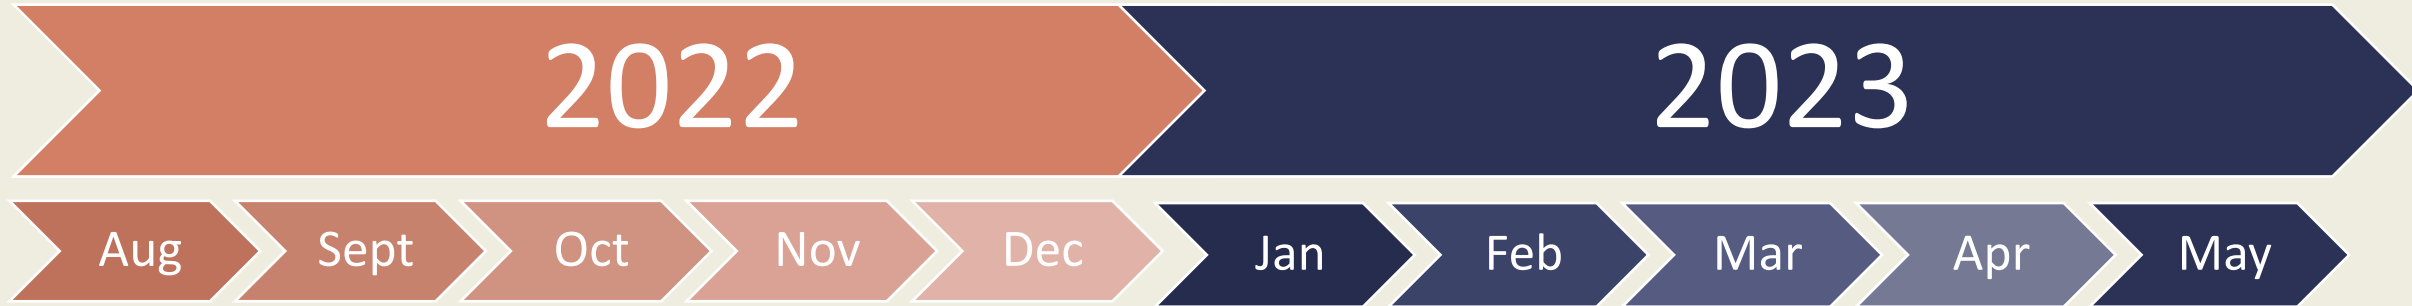

No lab nor biobank activities

Restart of activities

1<sup>st</sup> visitors



Preparation for the move



Physical transfer



Keys Ceremony







Opening of the NC



Inauguration



# Budget for the building (French authorities only)

Funding Partners	2015	2018	2021
French Government 	€17 million		
Auvergne-Rhône-Alpes Region 	€13 million	+€1.2 million	
Grand Lyon Metropole 	€18 million	+€1.2 million	+€7.8 million
City of Lyon 	Land + fonds de concours (decontamination)	+€1.2 million	
<b>Total</b>	<b>€48 million</b>	<b>€51.6 million</b>	<b>€59.4 million</b>

Grand Lyon Métropole is asking its partners to share the overcosts

# Budget for the equipment and physical move (to be paid by IARC)




Priority	Definition	Overall Costs As of 1/12/2021	Funds secured	Funds identified but not secured	Funding Gap
1	Critical item or earmarked donation	€6.76 million	€6.25 million	€0.51 million	-
2	Non-critical item, rebuilding existing capacity	€1.62 million	€0.03 million	-	€1.59 million
3	Investment in upstream sectors	€3.00 million	-	-	€3.00 million
<b>GLOBAL</b>		<b>€11.38 million</b>	<b>€6.27 million</b>	<b>€0.51 million</b>	<b>€4.59 million</b>

No more gap on priority 1 items.



Biobank – LN2 storage room – ventilation system

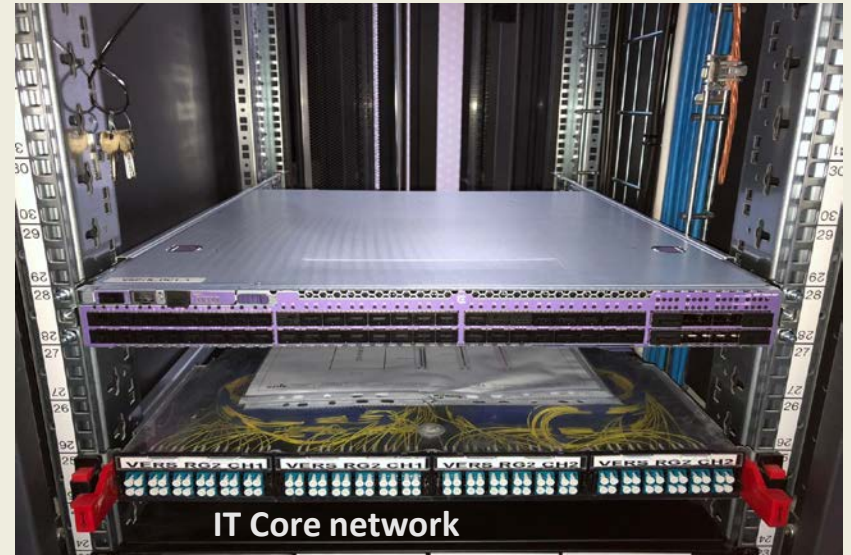


IT Core network



Internal staircase



Lab ventilation system

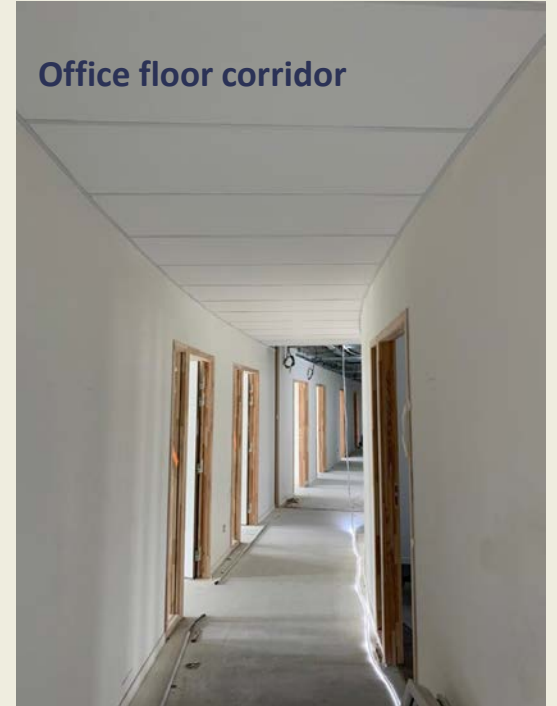

Office floor corridor

Outside view through the double façade system



View from the roof over Fourvière Hill



View of the South façade -  
Second skin under works









